BRUHAT BENGALURU M

	Clients Name	:	Executive Engineer Byatarayanapura Division
	Project Name	:	Package No.03(Package consists of 21 works)
	Consultants	:	Rudraprasad Consultants
	Project Manager /Team Leader	:	Karthik Rechan
	Project Start Date	:	22-Oct-18
	Project End Date	:	22-Oct-19
	Project Length in Months	:	12 months

Sl. No	*Assignment*	*Unit*	*Boq Qnty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*
1	Removing and refixing stone slabs of drains and pointing in CM (1:3) as per the directions of the Engineer-in-charge of the work .	Sqm	7079.30	5330.58	75	27-10-18	22-10-19	360
2	Providing granite slabs of selected quality roughly dressed havinf a size of 7.5 cms thick and fixed in cement mortar (1:6) including fixing curing etc.	Sqm	1375.59	891.36	65	28-10-18	22-10-19	359
3	Providing granite Slabs of Selected quality roughly dressed and fixed in cement mortor (1:6) including fixing curing etc..	Sqm	2251.18	187.08	8	28-10-18	22-10-19	359
4	Earthwork excavation by manual means in ordinary soil involving an average horizontal throw upto 2meters and an average lift upto 1.5 m, excavated surface leveled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications	Cum	8276.80	4853.14	59	26-10-18	22-10-19	300
5	Excavation for roadwork in soil with hydraulic excavator of 0.90 cum bucket capacity including cutting and loading in tippers, trimming bottom and side slopes, in accordance with requirements of lines, grades and cross sections, and transporting to embankment location and complete as per specifications	Cum	1648.43	820.89	50	27-10-18	22-10-19	360
6	Lead for disposal of earth shall be payable at Carriage rates (Lead & Lift) by mechanical means including loading and unloading up to 15kms	Cum	8276.80	5674.03	69	26-10-18	22-10-19	361
7	Construction of Embankment with Material Gravel/ Murrum. KSRRB M300-53. Construction of embankment with approved material Gravel/Murrum with all lifts and leads, transporting to site, spreading, grading to required slope and compacting to meet requirement	Cum	600.60	321.30	53	29-10-18	22-10-19	358
8	Providing,laying, spreading and compacting crushed stone aggregates of granite/trap/ basalt to wet mix macadam specification	Cum	1802.35	568.91	32	30-10-18	22-10-19	357
9	Scarifying bituminous course 50mm to 75mm thick along with premix carpet / surface dressing by road roller attached with scarifier without disturbing the base and stacking the debris	Sqm	6635.90	1201.20	18	01-11-18	22-10-19	355
10	Providing and applying primer coat with SS bitumen emulsion on prepared surface of granular Base such as WBM WMM including clearing of road surface and spraying prime	Sqm	11127.74	2472.13	22	03-11-18	22-10-19	353
11	Providing and laying dense graded bituminous macadam	Cum	210.78	59.99	28	04-11-18	22-10-19	352
12	Cleaning the existing black topped surface with brooms,soft brushes and finally dusting with old gunny bags and/or compressed air to receive bituminous	Sqm	104726.90	22174.89	21	06-11-18	22-10-19	350
13	Providing and applying tack coat using 80/100 grade bitumen (VG10) on prepared black topped surfaces at 2.5 Kg per 10 sqm, heating bitumen in boiler fitted with spray set	Sqm	114857.90	24648.02	21	08-11-18	22-10-19	348
14	Providing and laying bituminous concrete 30-40 mm compacted thickness with VG30 Bitumen grade using 40-60 HMP using crushed aggregates of grading II, premixed with bituminous binder	Cum	4743.08	986.52	21	08-11-18	22-10-19	348
15	Road Marking with Hot Applied Thermoplastic Compound with Reflectrising Glass Beads on Bituminous Surface	Sqm	4320.79	809.58	19	09-11-18	22-10-19	347

AHANAGARA PALIKE

RUDRAPRASAD CONSULTANTS BANGALORE

BRUHAT BENGALURU M

	Clients Name	:	Executive Engineer Byatarayanapura Division
	Project Name	:	Package No.03(Package consists of 21 works)
	Consultants	:	Rudraprasad Consultants
	Project Manager /Team Leader	:	Karthik Rechan
	Project Start Date	:	22-Oct-18
	Project End Date	:	22-Oct-19
	Project Length in Months	:	12 months

16	Cement concrete pavement.Construction of un-reinforced plain cement concrete pavement, thickness as per design, over a prepared sub base with OPC cement	Cum	905.27	376.30	42	27-10-18	22-10-19	360
17	Dismantling of existing structures like culverts, bridges, retaining walls and other structure comprising of masonry, cement concrete, wood work, steel work	Cum	426.14	266.59	63	24-10-18	22-10-19	363
18	Providing and laying in position plain cement concrete of mix 1:3:6 with OPC cement @ 220kgs, with 40mm and down size graded granite metal coarse aggregates	Cum	1184.76	777.04	66	26-10-18	22-10-19	361
19	Providing laying plain/ reinforced cement concrete M20 Grade for Box Drain walls of thickness 10cm to 20cm	Cum	1197.25	753	63	25-10-18	22-10-19	362
20	Providing TMT steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, palcing in position, lapping and / or welding wherever required.	tonne	63.03	42	66	27-10-18	22-10-19	360
21	Vaccum de-watering with vaccum pump and suction mat and compaction with skin floater clubbed with floating disc including cost of generator	Sqm	5556.35	3538	64	27-10-18	22-10-19	360
22	Providing and constructing granite size stone masonry in foundation cement mortor 1:6, stone hammered dressed in courses not less than 20cms high, bond stones at 2m	Cum	382.58	224	58	26-10-18	22-10-19	361
23	Providing and constructing granite / trap / basalt size stone masonry in basement with cement mortar 1:6, edges of stones chistle dressed in courses not less than 15 cms	Cum	108.57	67	62	26-10-18	22-10-19	361
24	Providing flush pointing to square rubble, course or uncoursed stone masonry with cement mortar 1:3	Sqm	773.59	628	81	26-10-18	22-10-19	361
25	Providing and laying in position plain cement concrete of mix 1:2:4 with cement @ 240kgs, with 20mm and down size graded granite metal coarse aggregates	Sqm	80.27	51	64	27-10-18	22-10-19	360
26	Providing and fixing pre cast solid cement concrete kerb stones made out of CC 1:2:4 with top and bottom width 114 and 165 mm respectively, 400mm high and 450mm in length	nos	3091.00	1235	40	10-11-18	22-10-19	346
27	Removing and resetting of footpath slab as per the directions of the Engineer-in-charge of the work .	Sqm	626.52	623	99	24-10-18	22-10-19	363
28	Dismantling of existing structures like culverts, bridges, retaining walls and other structure comprising of masonry, cement concrete, wood work, steel work, including T&P and scaffolding wherever necessary,	Sqm	27.36	26	96	24-10-18	22-10-19	363
29	Providing and constructing granite size stone masonry in foundation cement mortor 1:6, stone hammered dressed in courses not less than 20cms high, bond stones at 2m. apart in each course	Cum	41.04	41	100	26-10-18	22-10-19	361

WOR

AHANAGARA PALIKE

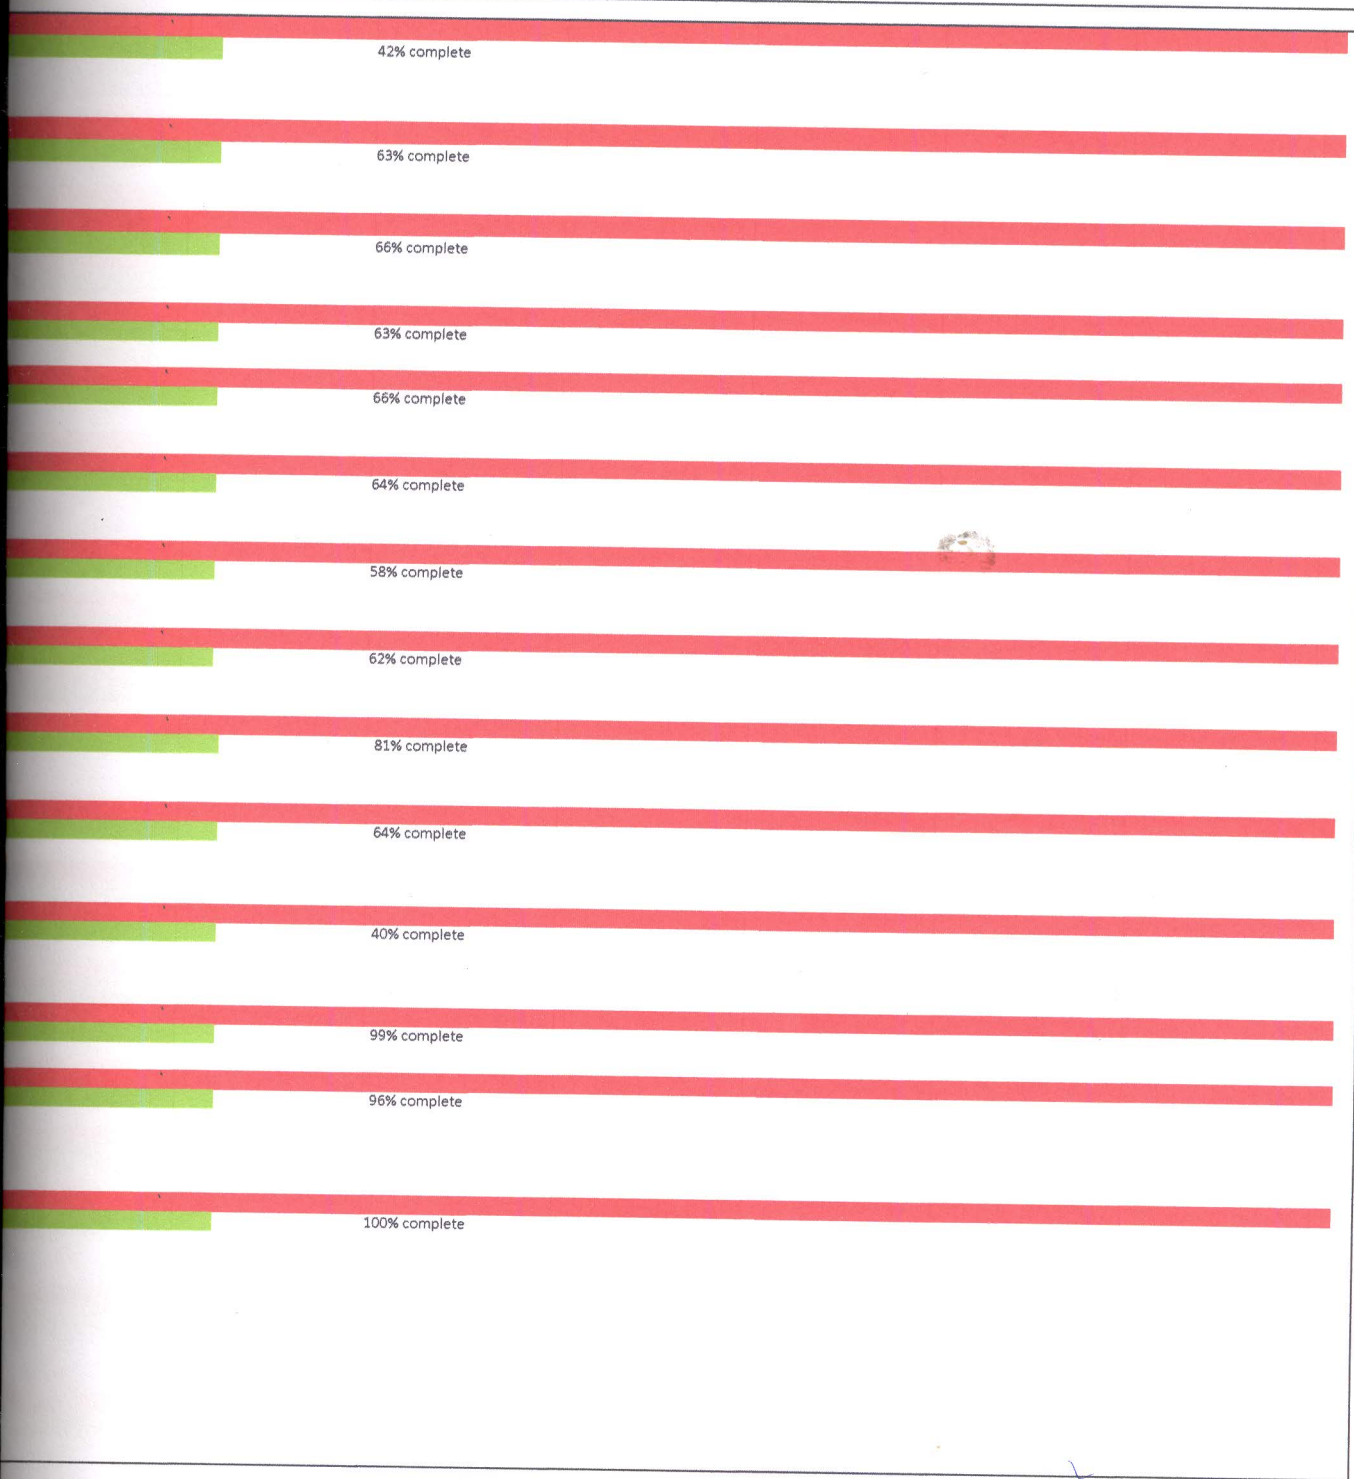

RUDRAPRASAD CONSULTANTS BANGALORE
